

North Sea Oil Platform Drill Tower Construction

Integrated EVM & Schedule Dependency Controls | Status Date: 2026-08-31

Runway & Burn

Project Manager

CFO Financials

Project Controller

Project Planner (Gantt)

1-Page Written Executive Project Status Report (Steering Committee Briefing)

Print / Save PDF

OFFSHORE EPC PLATFORM DRILL TOWER CONSTRUCTION PROJECT MONTHLY EXECUTIVE STEERING COMMITTEE STATUS BRIEFING

Status Date: August 31, 2026 (Month 8 / Week 36)

Prepared By: Frank Ellingsen, Lead Project Controller

Overall Project Health Status: 🚨 CRITICAL COST OVERRUN & SCHEDULE SLIPPAGE (RED) Budget Burn Out: Month 9 (Sep 2026)

1. KEY EVM PERFORMANCE METRICS

Metric	Value	Context / Threshold Info
Baseline Contract Budget (BAC)	\$26,500,000	Approved original baseline budget ceiling
Earned Work Complete (EV / BAC)	66.19% (\$17.54M)	66.19% of work scope accomplished to date
Planned Work Baseline (PV / BAC)	77.36% (\$20.50M)	77.36% of work baseline scheduled to date
Cumulative Actual Costs (AC)	\$23,440,000	Actual funds spent (exceeds EV by -\$5.90M)
Cost Performance Index (CPI)	0.7483	\$0.75 earned value generated for every \$1.00 spent (\$0.75 / \$1.00)
Earned Schedule Velocity (SPI)	0.9250	-18.2 Days behind baseline schedule progress
Critical Ratio (CR = CPI × SPI)	0.6402	Compound overall project health index (CPI 0.7483 × SPI 0.8556 < 0.90)

2. OUTTURN PREDICTIONS & P90 RISK

Scenario	EAC Outturn	Estimated Completion Date
Deterministic Base	\$35,413,604	Jan 31, 2027 (+31d)
Monte Carlo P50	\$34,060,783	Feb 27, 2027 (+57d)

Monte Carlo P90	\$35,815,202	Mar 14, 2027 (+72d)
* P90 Reserve Required: +\$401,598 above base EAC.		
3. PRIMARY VARIANCE DRIVERS		
Egersund Yard Rework (WBS 1.3.2): Pipe tolerance mismatch requiring 24/7 NDT welding (+\$2.40M / 26.9% of overrun). Time Delay Overhead Spread (\$SPI_t\$): Extending execution past Dec 31, 2026 spreads PMO & site overhead (+\$3.81M / 42.8% of overrun). Heavy Lift Vessel Weather Standby (WBS 1.4.1): Autumn sea-state vessel standby (+\$1.30M / 14.6% of overrun).		
4. REQUIRED STEERING COMMITTEE ACTIONS		
Authorize Overrun Credit Line: Secure +\$8.91M financing before September 15, 2026 (Month 9 budget exhaustion). Cap Yard Rework Billing: Transition Egersund yard to a fixed-fee labor cap for remaining mast assembly. Compress Offshore Hook-up: Recover 15 calendar days to preserve January 31, 2027 Commercial COD.		
Document ID: EVM-STR-2026-M08-REV3		Distribution: Executive Board & Steering Committee


AVG MONTHLY CASH BURN (M1-M8) \$2.93M / Mo Baseline Plan: \$2.56M/Month (+14.5% faster)	REMAINING BASELINE CAPITAL (\$BAC - AC) \$3.06M Remaining \$23.44M spent of \$26.50M budget	EXACT BUDGET BURN OUT MONTH Month 9 (Sep 2026) 100% of \$BAC budget ceiling exhausted	REQUIRED OVERRUN FINANCING (\$EAC - BAC) +\$8,913,604 Needs approval before Sep 15, 2026
---	---	---	--

 Cost Variance Waterfall Bridge (\$BAC → EAC Outturn Breakdown)

Original Budget: \$26.50M BAC

Total Overrun: **+\$8.91M VAC**


Outturn EAC: **\$35.41M**

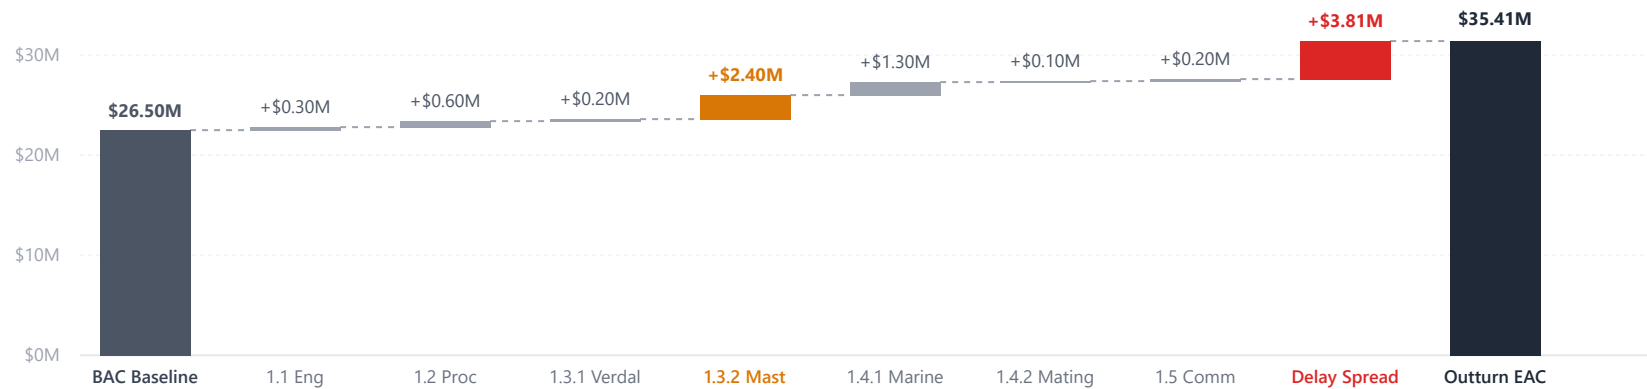

■ Original Baseline Budget (\$BAC) ■ Scope & Cost Overrun Steps ■ Primary Rework Driver (Egersund) ■ Time Delay Overhead Spread ■ Final Outturn Forecast (\$EAC)


Executive Donut Charts — Progress, Overrun & Budget Allocation

Physical Progress (\$EV / BAC\$)




● Earned **\$17.54M**
● Remaining **\$8.96M**

Cost Overrun Breakdown (+\$8.91M)



● Delay Overhead **42.8%**
● Egersund Mast **26.9%**
● Marine Standby **14.6%**

Baseline Budget Allocation (BAC \$26.50M)



● Fabrication **37.0%**
● Procurement **32.1%**
● Marine Ops **18.9%**

