

North Sea Oil Platform Drill Tower Construction

Integrated EVM & Schedule Dependency Controls | Status Date: 2026-08-31

Runway & Burn

Project Manager

CFO Financials

Project Controller

Project Planner (Gantt)

1-Page Written Executive Project Status Report (Steering Committee Briefing)

Print / Save PDF

OFFSHORE EPC PLATFORM DRILL TOWER CONSTRUCTION PROJECT MONTHLY EXECUTIVE STEERING COMMITTEE STATUS BRIEFING

Status Date: August 31, 2026 (Month 8 / Week 36)

Prepared By: Frank Ellingsen, Lead Project Controller

Overall Project Health Status: 🚨 CRITICAL COST OVERRUN & SCHEDULE SLIPPAGE (RED) Budget Burn Out: Month 9 (Sep 2026)

1. KEY EVM PERFORMANCE METRICS

Metric	Value	Context / Threshold Info
Baseline Contract Budget (BAC)	\$26,500,000	Approved original baseline budget ceiling
Earned Work Complete (EV / BAC)	66.19% (\$17.54M)	66.19% of work scope accomplished to date
Planned Work Baseline (PV / BAC)	77.36% (\$20.50M)	77.36% of work baseline scheduled to date
Cumulative Actual Costs (AC)	\$23,440,000	Actual funds spent (exceeds EV by -\$5.90M)
Cost Performance Index (CPI)	0.7483	\$0.75 earned value generated for every \$1.00 spent (\$0.75 / \$1.00)
Earned Schedule Velocity (SPI _t)	0.9250	-18.2 Days behind baseline schedule progress

2. OUTTURN PREDICTIONS & P90 RISK

Scenario	EAC Outturn	Estimated Completion Date
Deterministic Base	\$35,413,604	Jan 31, 2027 (+31d)
Monte Carlo P50	\$34,060,783	Feb 27, 2027 (+57d)
Monte Carlo P90	\$35,815,202	Mar 14, 2027 (+72d)

* P90 Reserve Required: +\$401,598 above base EAC.

3. PRIMARY VARIANCE DRIVERS

- **Egersund Yard Rework (WBS 1.3.2):** Pipe tolerance mismatch requiring 24/7 NDT welding (+\$2.40M / 26.9% of overrun).
- **Time Delay Overhead Spread (\$SPI_t\$):** Extending execution past Dec 31, 2026 spreads PMO & site overhead (+\$3.81M / 42.8% of overrun).
- **Heavy Lift Vessel Weather Standby (WBS 1.4.1):** Autumn sea-state vessel standby (+\$1.30M / 14.6% of overrun).

4. REQUIRED STEERING COMMITTEE ACTIONS

1. **Authorize Overrun Credit Line:** Secure +\$8.91M financing before **September 15, 2026** (Month 9 budget exhaustion).
2. **Cap Yard Rework Billing:** Transition Egersund yard to a fixed-fee labor cap for remaining mast assembly.
3. **Compress Offshore Hook-up:** Recover 15 calendar days to preserve January 31, 2027 Commercial COD.

Document ID: EVM-STR-2026-M08-REV3

Distribution: Executive Board & Steering Committee

AVG MONTHLY CASH BURN (M1-M8)

\$2.93M / Mo

Baseline Plan: \$2.56M/Month (+14.5% faster)

REMAINING BASELINE CAPITAL (\$BAC - AC)

\$3.06M Remaining

\$23.44M spent of \$26.50M budget

EXACT BUDGET BURN OUT MONTH

Month 9 (Sep 2026)

100% of \$BAC budget ceiling exhausted

REQUIRED OVERRUN FINANCING (\$EAC - BAC)

+\$8,913,604


Needs approval before Sep 15, 2026

Cost Variance Waterfall Bridge (\$BAC → EAC Outturn Breakdown)

Original Budget: \$26.50M BAC

Total Overrun: +\$8.91M VAC


Outturn EAC: \$35.41M

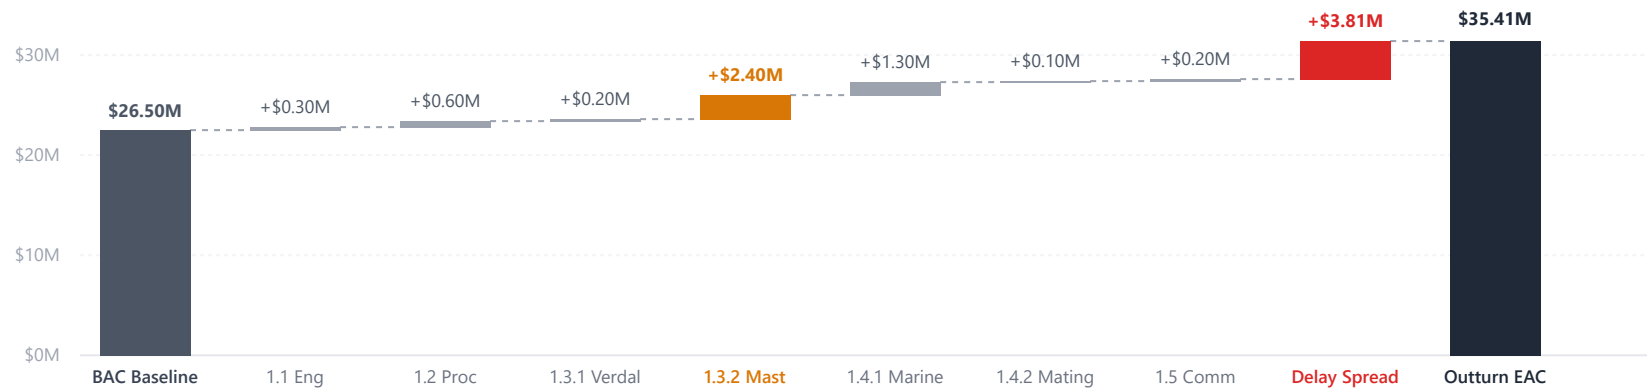

■ Original Baseline Budget (\$BAC) ■ Scope & Cost Overrun Steps ■ Primary Rework Driver (Egersund) ■ Time Delay Overhead Spread ■ Final Outturn Forecast (\$EAC)


Executive Donut Charts — Progress, Overrun & Budget Allocation

Physical Progress (\$EV / BAC\$)




● Earned \$17.54M
● Remaining \$8.96M

Cost Overrun Breakdown (+\$8.91M)



● Delay Overhead 42.8%
● Egersund Mast 26.9%
● Marine Standby 14.6%

Baseline Budget Allocation (BAC \$26.50M)



● Fabrication 37.0%
● Procurement 32.1%
● Marine Ops 18.9%

